

# Lewis River Aquatic Fund Projects (SA 7.5.3.2)

## Project Closeout Report

**Project Title:** Spencer Peak Road Decommission

**Project Approved By:** Aquatic Coordination Committee  
2009

**Original Project Sponsor:** USDA Forest Service

**Project Funding** \$33,000

**Project Description (work completed):**

- Closed 2.6 miles of road that drained into Clear Creek
- Removed 3 stream crossing culverts
- Removed 20 18" road drainage culverts
- Seeded and mulched all areas of ground disturbance
- Created 3 berms at beginning of road to block access
- Ripped first 200 feet of road

**Workforce:**

- **Personnel (by craft)**
  - USFS-project administrators-2
  - Machine operators-2
  - Contract labor-1
- **Contractors:**

**Schedule Summary:** Planned Completion Date: Summer 2010  
Actual Completion Date: July 2010

**Problems Encountered:**

- Could have used 2 excavators instead of one, or a bulldozer to help redistribute dirt away from creek crossings on larger culverts that had deep fill
- 

**Things that went well:**

- Contractor did a great job and was conscientious not to get dirt into creek when removing culverts.
- 

**Work Not Completed:**

- All work was completed.
-

**Lessons Learned:**

- Have two machines operating at the same time on deep culvert fills to remove dirt faster.

**\* Attachments (Photo Documentation):**

- 
- 

\*(Per National Marine Fisheries Service's Biological Opinion for Relicensing of the Lewis River Hydroelectric Projects):

Identify process or methodology the project will include and provide photo documentation of habitat conditions at the project site **before, during, and after** project completion.

- a. Include general views and close-ups showing details of the project and project area, including pre- and post-construction.
- b. Label each photo with date, time, project name, photographer's name, and documentation of the subject activity.

### 9300150 Road Decomission Project

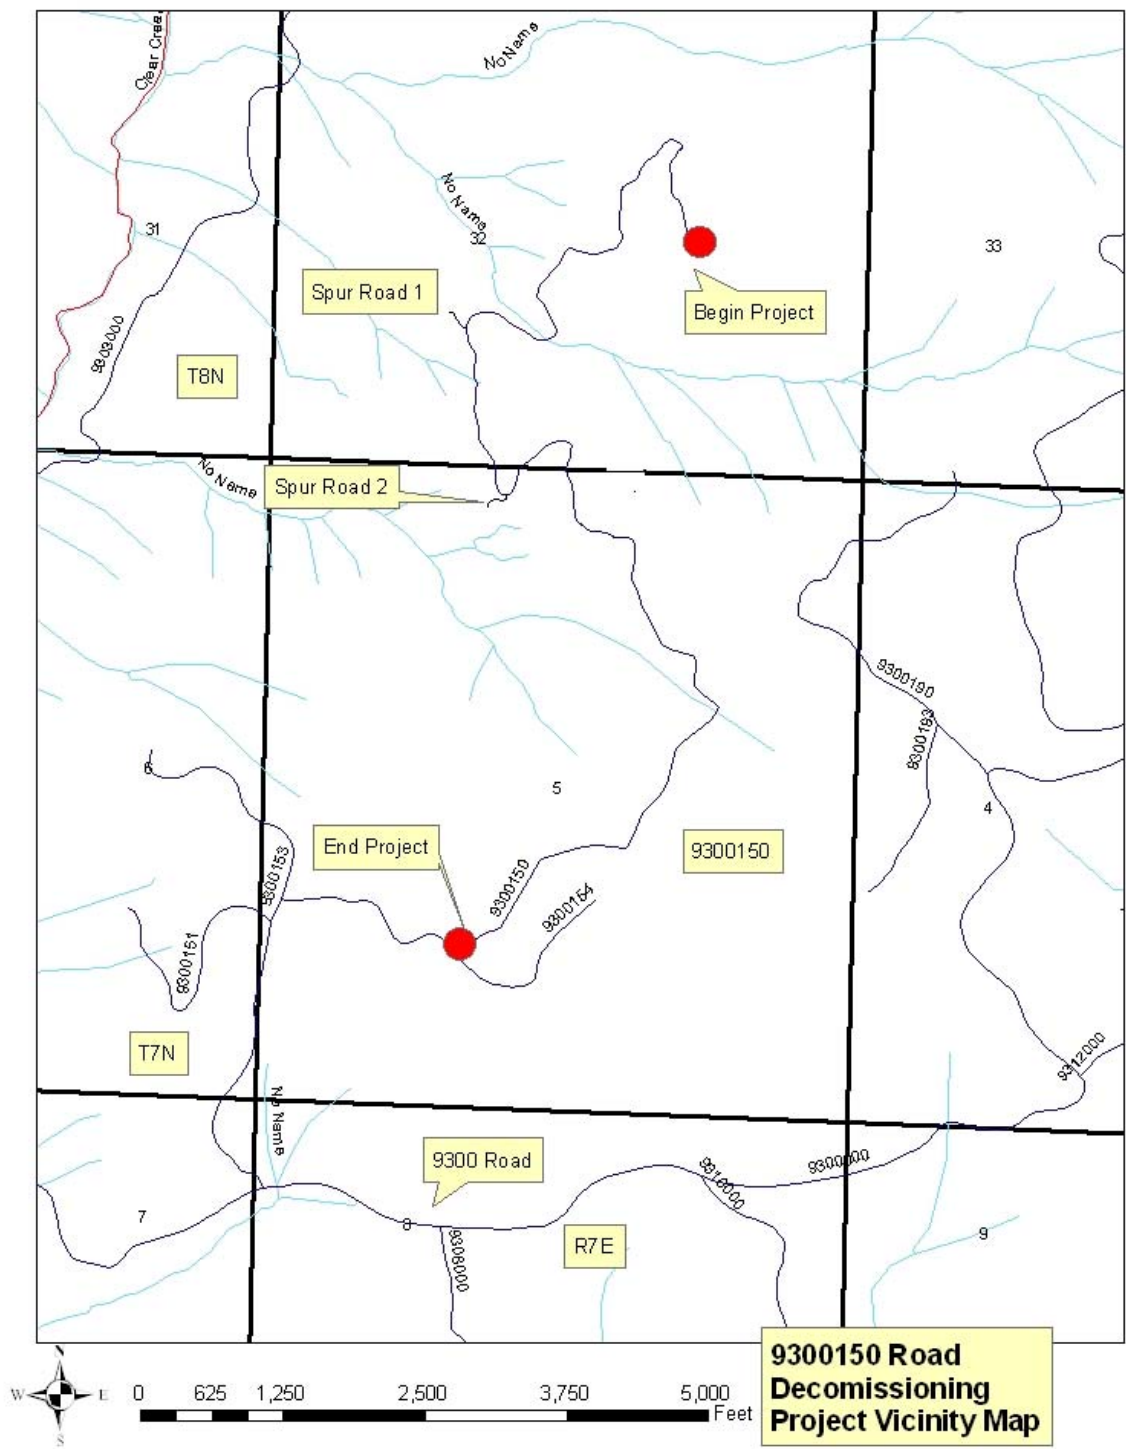


Figure 1. Map of road decommissioned



Picture 1. Large culvert prior to excavation, 9300150 road. Michaelis 7/19/2010



Picture 2. Largest culvert removed 9300150 road. Michaelis 7/20/2010
